



Annual Work Programme 2011

19 November 2010

Table of Contents

1.1	PURPOSE OF THE DOCUMENT	3
1.2	MISSION	3
1.3	2010 ACHIEVEMENTS	4
2.	THE PROGRAMME	6
2.1	PROGRAMME PLANNING, EXECUTION AND RELEASE DELIVERY	6
2.2	THE SESAR PROGRAMME RELEASE 1	9
2.2.1	Operational Package 1 Achievements	14
2.2.2	Operational Package 2 Achievements	14
2.2.3	Operational Package 3 Achievements	15
2.2.4	Operational Package 4 Achievements	18
2.2.5	Operational Package 5 Achievements	19
2.2.6	Operational Package 6 Achievements	20
2.3	WORK PACKAGE(S) AND PROJECTS ACTIVITIES WITH HORIZON BEYOND 2011	21
3.	SESAR PROGRAMME SPECIFIC ACTIVITIES IN 2011	23
3.1	ATLANTIC INTEROPERABILITY TO REDUCE EMISSION (AIRE)	23
3.2	WORK PACKAGE E.....	25
3.3	OPTIMI AND SAT OPTIMI	26
3.4	ATM MASTER PLAN UPDATE	26
3.5	MILITARY.....	27
3.6	PROFESSIONAL STAFF ASSOCIATION.....	28
3.7	NATIONAL SUPERVISORY AUTHORITIES.....	28
4.	COORDINATION WITH OTHER PROGRAMMES AND ORGANISATIONS	29
4.1	FAA/NEXTGEN	29
4.2	CLEAN SKY	30
4.3	FRAMEWORK PROGRAMME (FP) PROJECTS.....	30
4.4	ICAO	30
4.5	EASA	31
4.6	ESA.....	31
4.7	EXTERNAL RELATIONS	31
5.	COMMUNICATION PLAN	32
6.	ADMINISTRATION & FINANCE	32
6.1	ENSURE EFFICIENT SUPPORT TO THE PROGRAMME IMPLEMENTATION.....	32
6.2	ON TIME ASSESSMENT OF CONTRACTUAL DELIVERABLES AND PROJECT'S INTERIM REPORT.	33
6.3	ENSURE EFFECTIVE IMPLEMENTATION OF ICS AND RISK MANAGEMENT.....	33
6.4	SET UP PROGRAMME'S FINANCIAL AUDIT STRUCTURE.....	34
7.	INTERNAL AUDIT	35
7.1	INTERNAL AUDIT WORK PROGRAMME 2011	35
7.2	CHANGES TO THE SJU INTERNAL AUDIT ARRANGEMENTS IN 2011	35
7.3	ASSURANCE WORK	35
7.4	CONSULTING AND OTHER WORK	35
7.5	CO-ORDINATION AND OVERSIGHT OF PUBLIC AUDIT FUNCTIONS	35
7.6	RESOURCES	36
8.	GLOSSARY	37
9.	ANNEXE I - PROJECTS (EXCLUDING RELEASE 1) IN EXECUTION PHASE - 2011 PLANNED DELIVERY	38
10.	ANNEXE II - PROGRAMME FINANCIALS.....	38

1.1 Purpose of the document

The purpose of the Annual Work Programme is to outline the activities that will be performed by the SESAR Joint Undertaking (hereinafter the SJU or Joint Undertaking) in 2011 and its expected achievements contributing to the 2012 mid-term strategic objectives. It describes how the resources made available by the European Union, Eurocontrol and the Members will be geared towards the 2011 achievements by detailing the operational and administrative actions that will be performed during the year.

1.2 Mission

The SJU is established by Council Regulation (EC) 219/2007, as last modified by Council Regulation (EC) 1361/2008. The aim of the SJU is to ensure the modernisation of the European air traffic management system by coordinating and concentrating all relevant research and development efforts in the European Union. It shall be responsible for the execution of the ATM Master Plan and in particular for carrying out the following tasks:

- organising and coordinating the activities of the development phase of the SESAR project in accordance with the ATM Master Plan, by combining and managing under a single structure public and private sector funding,
- ensuring the necessary funding for the activities of the Development phase of the SESAR Programme in accordance with the ATM Master Plan,
- ensuring the involvement of the stakeholders of the air traffic management sector in Europe, in particular: air navigation service providers, airspace users, professional staff associations, airports, and manufacturing industry; as well as the relevant scientific institutions or the relevant scientific community,
- organising the technical work of research and development, validation and study, to be carried out under its authority while avoiding fragmentation of such activities,
- ensuring the supervision of activities related to the development of common products duly identified in the ATM Master Plan and if necessary, to organise specific invitations to tender.

Based on the above, the management of the SJU has established a mid-term “vision” to ensure that the results reached and progress made towards the achievement of the SJU mission are concretely measurable and monitored during the overall duration of the Programme, so that:

By 2012 we have created the change in the European ATM that demonstrates our ability to deliver benefits to the community

The strategic objectives set for the end of 2012 are:

- initial 4D trajectory is validated in an operational environment supported by satellite-based technology,
- 10,000 flights, including 500 military, are SESAR labelled,
- 80% of SESAR projects have tested their output in a real life environment,
- first SWIM pilots are in place to exchange data across at least 5 domains,
- the first remote tower is ready for operations,

- SESAR benefits are demonstrated on city pairs connecting 8 European airports,
- airspace users have signed up to the SESAR business case for time-based operations.

1.3 2010 achievements

Following the launch of the SESAR Programme activities in June 2009, the following key achievements, which have an impact on the planned 2011 activities, need to be mentioned:

- a. at the end of October 2010, 275 projects were initiated and 217 entered the execution phase; the integration of activities awarded as part of IBAFO II is well on its way and around 1800 persons are currently involved in the different projects of the SESAR Programme. The Programme activities are developing as planned and constitute a solid basis to be further progressed to contribute to the 2012 strategic objectives' achievement.
- b. in June 2010, the first Engineering Review Session, i.e. the assessment of the progress of the different Work Packages/Projects towards the SJU Targets, was performed. In particular, the review highlighted how the critical dependencies have been established and contribute to the coherent progressing of the projects towards the Targets as well as the need for some corrective actions to align schedules, content, and engineering methodology (see 2.1);
- c. with regard to the Programme reporting, the SJU has introduced a structured quarterly reporting based on effort consumption that shall be submitted by the Members, starting with quarter III 2010. This report will provide the SJU with an additional monitoring of the alignment of the Members' efforts with the programme objectives, and of the risk incurred;
- d. with regard to Validation, SESAR partners found an agreement on a V&V¹ roadmap, which in particular stresses the importance of being as close as possible to the real operational environment in all validation activities;
- e. WPE (Long Term Research, see also 3.2) and WP11 (Flight Operations Centre Systems) have been launched and activities are expected to start fully respectively by year end and by the first quarter 2011;
- f. in order to ensure the involvement of all stakeholders in the Programme, the SJU has assured their participation through the award of contracts as a result of procurement procedures, directly or through Eurocontrol:
 - during the first months of 2010 a contract was signed to add "low cost airspace users" expertise. The amount committed during 2010 is of EUR 1.5 million;
 - with regard to the involvement of the Military, more and more contacts are developed with the different National Defence administrations and through Eurocontrol DCMAC. The recruitment of a Senior Military Advisor in May 2010 has

¹ Validation & Verification

- substantially accelerated the awareness process of SESAR within the Military community (see 3.5);
- the involvement of the Professional Staff Associations has been assured through the signature by Eurocontrol on behalf of the SJU of 5 contracts with each of the associations (see 3.6). The amount committed for the period 2010 - 2012 is of EUR 1 million as cash contribution of Eurocontrol. The administration and payments are managed by Eurocontrol, once the deliverables are approved by the SJU;
- g. the second phase of AIRE (Atlantic Interoperability Initiative to Reduce Emissions) procurement procedure was launched and completed, resulting in the award of 18 contracts with different consortia in charge of the performance of the activities (see 3.1). The total amount committed is EUR 2.7 million;
 - h. a study on wireless communication was launched by the SJU in May 2010 and 2 contracts for the amount of EUR 0.5 million were signed;
 - i. following the initialling of a MoC between the EU and the FAA, the SJU in cooperation with the EC and Eurocontrol will establish the most appropriate framework to implement this memorandum in concrete activities (see 4.1). In this respect, it is the intention of the SJU to ensure that its Members involved operationally at Project level are focal points with their USA correspondents in the different relevant domains. Furthermore, external relation in co-operation with the EC and Eurocontrol were established with different strategic areas around the world, in particular Brazil, China, India and the Middle East countries (see 4.7);
 - j. the communication plan has been implemented in accordance with the Budget approved by the Administrative Board (see 5). Within the effective activities performed by the Communication team, the annual Amsterdam Global ATC conference in March constitutes an example of efficient and effective results within contained resources;
 - k. almost all 2010 administrative and financial objectives were achieved by the end of August 2010. In particular, the successful implementation of ABAC and SAP was completed in May 2010, while “ABAC Contract Module” will be implemented by year end. On the contrary, following a discussion with DG BUDG, “ABAC Assets Module” will not be implemented and instead SAM (SAP Assets Management) will be implemented during 2011 as soon as available;
 - l. with regard to Project Audit, two project auditors were recruited and started respectively on August 1st and September 1st 2010. The Audit strategy has been defined and implementation is ongoing with the first batch of audits to be performed starting at year end, beginning of 2011. A framework contract for audit services was signed, after an open procurement procedure, with Ernst and Young in May 2010 (see 6.4);
 - m. the overall SJU recruitment process is almost completed, having only two vacant positions for which recruitments are ongoing;

- n. during the first 10 months of 2010, the SJU has disbursed EUR 29.5 million in terms of pre-financing. In the last two months pre-financings totalling EUR 43 million are planned, bringing the total amount of pre-financing paid by the SJU up to EUR 126.6 million;
- o. requests of co-financing related to the eligible costs incurred by Members during 2009 have been received totalling EUR 2.4 million². Internal assessment is completed and disbursements are ongoing within the provisions of the MFA;
- p. the Eurocontrol contribution to the SJU for 2009 is EUR 9 million cash, EUR 8.0 million activities realized by Eurocontrol on behalf of the SJU (early projects, ISA, secondments) and EUR 11.5 million in-kind, in the final stage of the validation process.

The draft Annual Activity Report for 2010, which an extensive description of all the results achieved will be submitted to the Administrative Board by the end of January 2011, while the final version is due by the end of March 2011.

2. The Programme

2.1 Programme planning, execution and release delivery

During 2010 a comprehensive review of the SESAR Programme implementation approach was conducted and included the V&V roadmap as well as the lessons learnt from the System Engineering process. The conclusions of the review highlighted the need to breakdown the Programme high level objectives into a more technical and operational level defining in detail what has to be done, by whom and when, and thus to clearly identify the SESAR validated deliverables which will contribute to the SESAR Development Phase objectives as well as to the specific 2012 Strategic Objectives.

The Programme review identified critical project dependencies as well as the first common deliveries to be completed in 2011 and 2012. Furthermore, the lessons learnt from the first application of the System Engineering processes suggested that a more efficient approach was required.

As a result of this comprehensive exercise, the SJU and the Members agreed that the most appropriate way to deliver consisted in articulating the Programme Plan through SESAR Releases contributing to the development of the SESAR Storyboard Steps. The first SESAR Release is due by year end 2011 and it will be followed by Releases with annual frequency or every two years, the content of which will be defined based on the level of maturity of the different Projects.

² It should be noted that the costs eligible for co-financing during 2009 were limited to those related to the completed deliverables - in this case the PIRs and RCAs for the Projects for which the SJU decided the launch of the execution phase. This excluded all the costs related to the Work in Progress related to the remaining Projects. As a result, the amount of the co-financing for 2009 does not represent the complete work done by the Members during the year. In order to ensure a more appropriate alignment of the co-financing with the work realized, the MFA has been amended to include in the eligible cost of each financial year the Work in Progress too.

A SESAR Release embeds groups of projects delivering, in a determined timeframe, R&D results that can support decision to move related activities to the industrialisation stage (end of V3).

Each Release is developed through 3 phases (see fig.1):

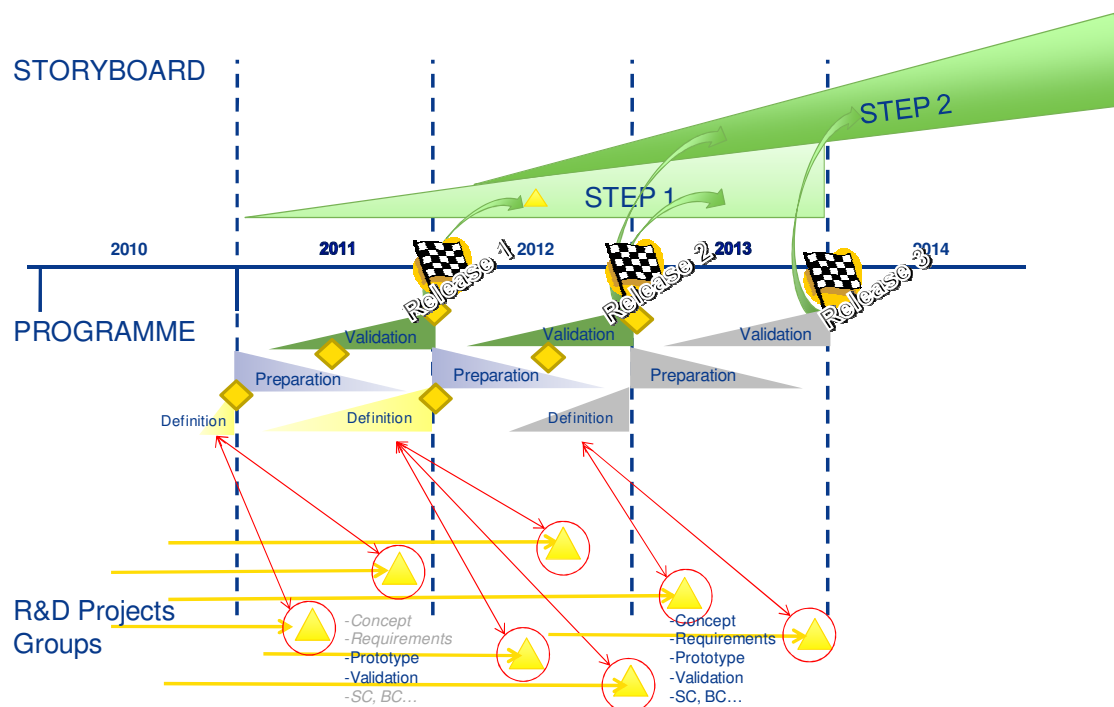


Figure 1: SESAR Programme Plan

- **Definition:** this phase aims at defining the Release scope and at getting the commitment of all the involved SESAR members to the Release plan. Defining a Release is a continuous process assessing the project ability to deliver for the considered deadline. This assessment is based upon the projects plans and projects inputs and, later, on the validation reports from previous Releases. At the end of this phase:
 - projects included in the release have clarified their objectives and demonstrated through a realistic & achievable plan their ability to deliver within the following period,
 - assessment of the Release coherence has been performed with regards to project dependencies and high level operational and technical objectives,
 - all projects participating to the Release have committed upon the Release plan.
- **Preparation:** this phase aims at preparing the V&V Exercise execution, i.e. developing the pieces of concept description and solution (system and/or procedures) that are due for the on-going release. At the end of this phase:
 - requirements have been captured,
 - prototypes have been developed and verified by the project in charge of their development,

- prototypes are integrated to the IBPs (Industry Based Platforms) on the validation site,
 - integration platforms have been qualified for the execution of integrated validation activities,
 - V&V exercises are defined and planned.
- Validation: this phase aims at validating the pieces of solution developed for the Release and assessing their maturity in order to determine whether it is possible to move to the following phases of the European Operational Concept Validation Methodology (E-OCVM) (V4). During this phase:
 - V&V Exercises are executed,
 - Operational concept and technical solutions are documented.

The progress towards the delivery of the SESAR Release is controlled at Programme level through System Engineering (SE) Reviews. These SE Reviews take place:

- at the end of the Release Definition Phase,
- at the end of the Release Preparation Phase,
- at the end of the Release Validation Phase.

Even though it is acknowledged that not all activities progress at the same pace, for efficiency reasons, SE Reviews are organised at a fixed time of the year.

In parallel to the current Release execution activities, Primary projects which are not considered for the current Release:

- follow their project plan aligned with the E-OCVM methodology and are controlled through the project gates,
- contribute to the definition of further releases.

Progressively, projects will be making the necessary steps towards the validation of the SESAR concept of operation: establishment of the operational requirements, development and verification of the prototypes and ultimately the conduct of validation activities.

The Release delivery process has been structured around a set of 6 Operational Packages and associated Sub-Packages clustering projects and activities based on their outputs and ensuring an operational and performance focus.

Two technical packages have been defined to structure technology that has a wide operational coverage; CNS and SWIM (see fig.2).

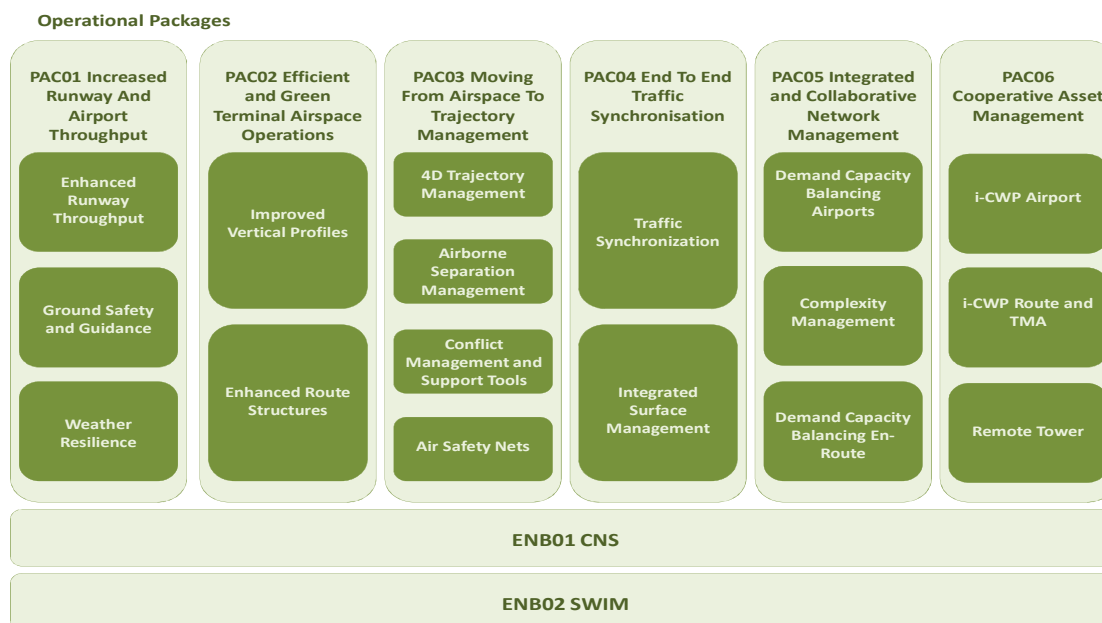


Figure 2

An **Operational Package** is a deployment focused grouping of operational changes and associated technical and procedural enablers.

An **Operational Sub-Package** is a sub-grouping of connected operational and technical improvements related to the Operational Package and comprising a sub-set of Operational Improvements (OIs) with closely related operational focus, designed to meet performance expectations of the ATM Master Plan.

To ensure that both Operational and Technical projects are structured in a way that dependencies are respected and that common work areas lead to coherent and integrated set of validation results, a third grouping based on common focus and linked to the Operational Sub-Packages was defined as Operational Focus Area

In this respect, an **Operational Focus Area** is a limited set of dependent operational and technical improvements sitting within an Operational Sub-Package, comprising specific interrelated OIs designed to meet specific performance expectations of the ATM Performance Partnership.

2.2 The SESAR Programme Release 1

In 2011, close to 260 projects will be in full execution mode delivering the first R&D results as well as the necessary guidance material to the Programme, in particular for the establishment of the various *cases* (safety, business, security, environment, human factors). In addition, after having been involved in the initiation phase, Airspace Users experts have been allocated to the various projects with clear contributions identified for 2011. Their output as well as their feedback on the progress of the Programme will be

assessed by the SJU on a quarterly basis. Equally all Staff Associations experts have been allocated to various projects as well as to validation exercises by establishing an International Validation Team of operational experts across the ATM domains, e.g. controllers, engineers and pilots.

The figure here below, Figure 3, identifies through the aforementioned three layers, the Operational Focus Areas within which projects will provide validated deliverables (see the following sections 2.2.1 to 2.2.6 for details).

Operational Package	Operational Sub-package	Operational Focus Area	Delivery
PAC01 Increased Runway and Airport Throughput	Weather Resilience	LVPs using GBAS Pilot synthetic vision	
	Ground Safety and Guidance	Ground safety nets Enhanced situational awareness Runway Status Lights (RWSL) Guidance assistance to aircraft and vehicles	
	Enhanced Runway Throughput	Time Based Spacing Dynamic Vortex Spacing Brake to Vacate	
PAC02 Efficient and Green Terminal Airspace Operations	Enhanced Route Structures	Optimised RNP Structures Point Merge in Complex TMA	2011 2011
	Improved Vertical Profiles	i4D + CDA + AMAN in Medium Complex TMA A-CDA A-CCD Arrival Procedure with Vertical Guidance	2011
PAC03 Moving from Airspace to Trajectory Management	4D Trajectory Management	i4D IOP + i4D Free Routing SBT and RBT, with automated support OAT trajectories Authorisation & revision using data link Cruise climb System interoperability and data sharing	2011
	Airborne Separation Management	ASPA S&M ASPA S&M integrated with AMAN ATSA-ITP	
	Conflict Management and Support Tools	Conflict detection and trajectory conformance monitoring Conflict resolution Enhanced Decision Support Tools and Performance Based Navigation Sector team operations Generic controller validations	2011

Operational Package	Operational Sub-package	Operational Focus Area	Delivery
		MSP (Multi Sector Planning)	2011
	Air Safety Nets	Enhanced STCA ACAS	2011 2011
PAC04 End to End Traffic Synchronisation	Traffic Synchronization	Integrated AMAN DMAN Extended AMAN horizon AMAN + Point Merge in Complex TMA DMAN Multiple Airports i4D + CTA AMAN	2011 2011 2011
	Integrated Surface Management	Surface Routing Surface movement and planning Surface management Integrated with Arrival & Departure Management	
PAC05 Integrated and Collaborative Network Management	Demand Capacity Balancing Airports	Airport Operations Plan (AOP) Airport CDM	
	Complexity Management	Complexity Assessment and Initial Complexity Resolution	2011
	Demand Capacity Balancing En-Route	AFUA/ ASM Military and Civil Interoperability Dynamic sectorisation and Constraint management Enhanced DCB and dynamic DCB processes Digital NOP UDPP NOP	2011
PAC06 Cooperative Asset Management	iCWP Airport	iCWP Airport	2011
	iCWP Route and TMA	iCWP Route and TMA	2011
	Remote Tower	Remote Tower	2011
ENB01 CNS	CNS	CNS AeroMACs	
ENB02 Information Management	SWIM	TBD	

Figure 3

A clear representation of the link between the 2011 activities and expected achievements and the 2012 strategic objective is provided below.

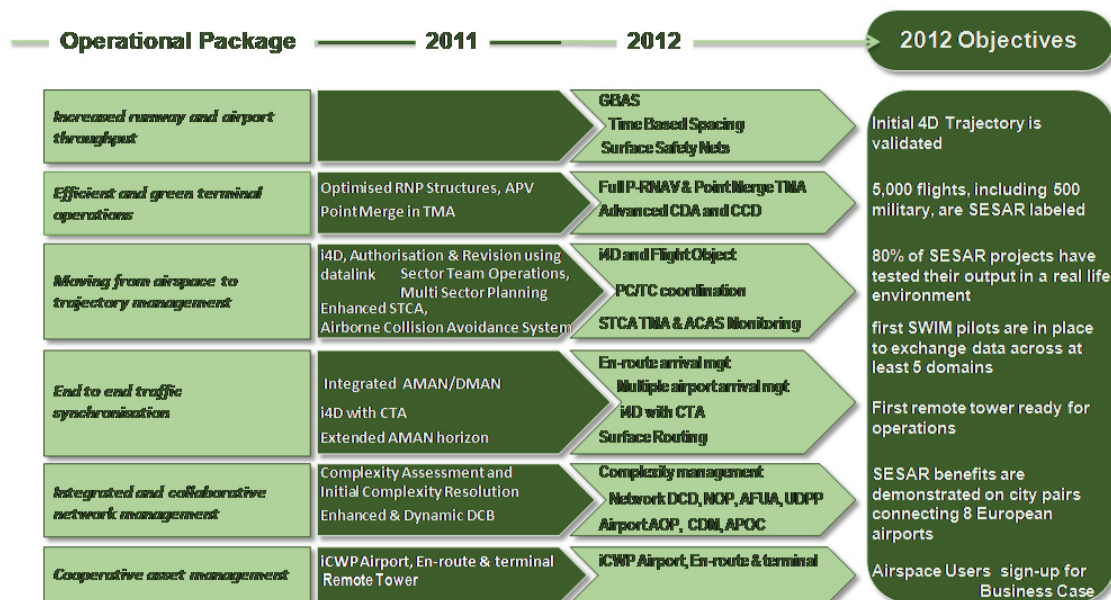


Figure 4: Contribution to the 2012 Objectives

In November 2010 the SJU and the Members involved in the Programme agreed on 27 exercises within 17 Operational Focus Areas to be performed and completed as described hereafter (see sections 2.2.1 to 2.2.6), whereas discussions are still ongoing on 4 additional exercises. This set of Operational Focus Areas and associated validation exercises represent the scope of the Release 1, which consists of a total effort estimated at 3 000 Men*months or around EUR 37.3 million³.

Release 1 consists of the package of work having completed the V3 and on which a decision for industrialisation and subsequent deployment can be made. The locations of the Release 1 validation activities are illustrated on Figure 5.

³ Estimated at EUR 12.418 Men*months as per IBAFO.

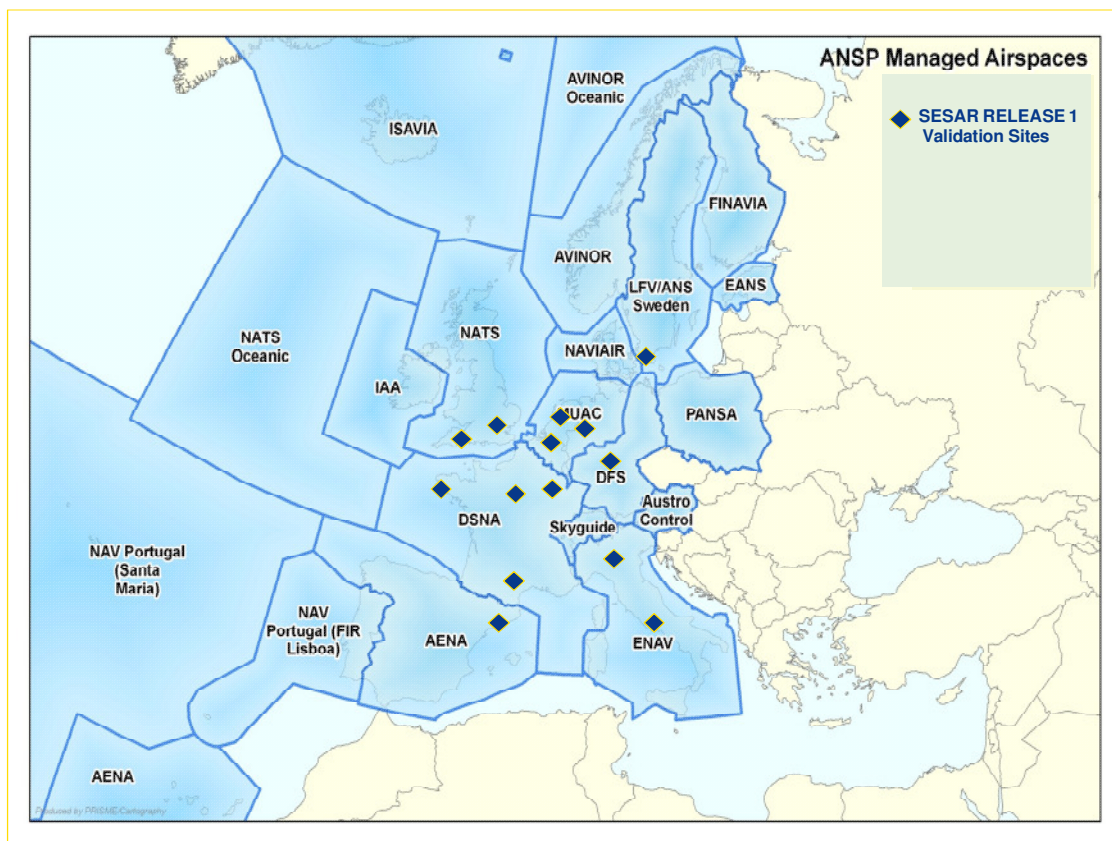


Figure 5: Main locations of the Release 1 Validation activities

The projects activities identified as part of Release 1 are described in the Release Plan. The execution of this plan will be closely monitored by the SJU and regular reports will be provided to the governance of the Programme. During the definition, preparation and validation phases of the Release, projects are subject to System Engineering reviews organised by the Industrial Support. Together with the System Engineering methodology applied in 2011, this work will deliver periodical assessment of the level of maturity achieved in the Programme. It will ensure as well technical consistency of the various activities and outputs, together with the formalisation and traceability of the requirements. This approach is particularly important for the identification and establishment of the future standards

2.2.1 Operational Package 1 Achievements

PAC01 Increased Runway and Airport Throughput

No Exercise in Release 1 is identified for PAC01.

2.2.2 Operational Package 2 Achievements

PAC02 Efficient and Green Terminal Airspace operations

Optimised RNP Structures			
Achievement	Validated procedures, requirements, cases and updated P-RNAV Guidelines- on PRNAV in complex TMA		V3
Deliverables	OSED ⁴ , SPR ⁵		
Contributing Project	5.7.4		
Estimated Efforts	45 Men*months		
Exercise	Validation Technique	Platform	Exercise Completed
EXE-05.07.04-VP-142	RTS ⁶	AENA Barcelona TMA	June 2011

Point Merge in Complex TMA		
Achievement	Validated Point Merge - procedures based on and exploiting the Flight Management System (FMS) without radar vectoring, constrained by controller instructions on speed and level, requirements and cases It will Facilitate the application of Continuous Descent Arrival and provide a baseline for Trajectory Based operations in the TMA	V3
Deliverables	OSED, SPR, INTEROP ⁷ , Technical Specifications, Validation Report	
Contributing Projects	5.7.4	

⁴ OSED = Operational Service Environment Description is a document detailing Concept description for each Operational Focus Area. It develops the addressed Operational Service by allocating Operational Requirements to Operators, Application Services and Information Services.

⁵ SPR = Safety and Performance Requirements is a document detailing the OSED for each Operational Focus Area in allocating Operational, Safety and Performance requirements to Systems.

⁶ RTS: Real Time simulation, using an operational platform.

⁷ INTEROP = Interoperability is a document providing interoperability requirements which are the minimum technical and functional requirements that provide the basis for ensuring compatibility among the various elements of the technical systems supporting defined services and using specific technology

Estimated Efforts	45 Men*months		
Exercise	Validation Technique	Platform	Exercise Completed
EXE-05.07.04-VP-228	RTS	ENAV Milan TMA	December 2011
EXE-05.07.04-VP-229	RTS	NATS TC London TMA	December 2011

Arrival Procedure with Vertical Guidance			
Achievement	Validated Approach Procedures with Vertical (APV) guidance using Satellite Based Augmentation System (SBAS) leading to the ability to fly Instrument Landing System (ILS) type approaches to airport independently of ground based infrastructure.		V3
Deliverables	OSED, SPR, Technical Specifications, Validation report		
Contributing Projects	5.6.3		
Estimated Efforts	87 Men*months		
Exercise	Validation Technique	Platform	Exercise Completed
EXE-05.06.03-VP-224	RTS	NATS TC Southampton APT	October 2011
EXE-05.06.03-VP-297	RTS	ENAV	September 2011

2.2.3 Operational Package 3 Achievements

PAC03 Moving from airspace to trajectory Management

i4D			
Achievement	Initial procedures and requirements for initial 4 Dimensions (i4D) concept for supporting the management of a single Controlled Time Arrival (CTA) constraint in the En-Route and TMA phase of flight.		V3
Deliverables	OSED, SPR, INTEROP		
Contributing Projects	4.5; 5.5.1		
Estimated Efforts	86 Men*months		
Exercise	Validation Technique	Platform	Exercise Completed

EXE-04.05-VP-041	RTS En-route	ENAV Rome	October 2011
EXE-05.05.01-VP-212	RTS En-route	ENAV Rome	October 2011

Authorisation & revision using data link

Achievement	Validated procedures, requirements, cases for Trajectory Management revision considering : Flow rerouting scenario and unexpected closure of airspace		V3
Deliverables	OSD, SPR & Validation report		
Contributing Projects	4.5		
Estimated Efforts	138 Men*months		
Exercise	Validation Technique	Platform	Exercise Completed
EXE-04.05-VP-043	RTS	DSNA Coflight Toulouse	December 2011

Sector team operations

Achievement	Validated procedures, requirements and enhanced cooperating tools to improve sector team organisation and coordination (roles & responsibilities)		V3
Deliverables	OSD, SPR, INTEROP, Technical Specifications, Validation report		
Contributing Projects	4.3		
Estimated Efforts	237 Men*months		
Exercise	Validation Technique	Platform	Exercise Completed
EXE-04.03-VP-032	Shadow mode	Brest ATCC	December 2011
EXE-04.03-VP-237	Live Trials	Brest ATCC	December 2011

Multi Sector Planning

Achievement	Initial multi-sector planner operating environment (roles & responsibilities), with initial definition of tools support and information sharing		V3
Deliverables	SPR.		
Contributing Projects	4.7.8		

Estimated Efforts	90 Men*months		
Exercise	Validation Technique	Platform	Exercise Completed
EXE-04.07.08-VP-304	RTS	NATS London ACC Ops room platform	October 2011

Enhanced STCA			
Achievement	Validated procedures, requirements, prototype and cases for enhanced Short Term Conflict Alert (STCA). This enhanced STCA will a) support controllers to identify conflicts between flights inside TMA where difficult operations are conducted (e.g. IFF/VFR traffic, complex interface with arrival/departure sectors, etc) and b) to avoid false alarms.		V3
Deliverables	OSED, SPR, INTEROP, Technical Specifications, Validation report		
Contributing Projects	4.8.1; 10.4.3		
Estimated Efforts	97 Men*months		
Exercise	Validation Technique	Platform	Exercise Completed
EXE-04.08.01-VP-140	RTS	THALES STCA prototype	December 2011

Airborne Collision Avoidance System			
Achievement	Validated procedures, requirements, prototype and cases for : - new altitude capture laws to avoid false alarm in high vertical rate encounter, - link Airborne Collision Avoiding System to autopilot, and - quantified overall safety gain.		V3
Deliverables	OSED, SPR, INTEROP, Technical Specifications, Validation report		
Contributing Projects	4.8.2		
Estimated Efforts	77 Men*months		
Exercise	Validation Technique	Platform	Exercise Completed
EXE-04.08.02-VP-054	TBC	DSNA Toulouse	February 2011
EXE-04.08.02-VP-480	TBC	DSNA Toulouse	February 2011

2.2.4 Operational Package 4 Achievements

PAC04 End to End Traffic Synchronisation

Integrated AMAN/DMAN			
Achievement	Validated procedures, requirements, prototypes and cases for coupled Arrival Manager (AMAN) and Departure Manager (DMAN) capabilities at a single airport. Validation of procedures for establishing the departure (take-off) sequence with sufficient quality taking into account surface and departure management processes. The validation will include the baseline DMAN requirements.		V3
Deliverables	OSED, SPR, INTEROP, Technical Specifications, Validation report		
Contributing Projects	6.8.4		
Estimated Efforts	69 MEN.MONTHS		
Exercise	Validation Technique	Platform	Exercise Completed
EXE-06.08.04-VP-470	Life Trial	DSNA CDG	March 2011

Extended AMAN horizon			
Achievement	Initial procedures on extending the arrival tasks to the En-route controllers within Arrival Manager (AMAN) horizon of a related airport.		V3
Deliverables	OSED, SPR, INTEROP, Validation report		
Contributing Projects	4.5; 5.5.1; 5.6.1; 5.6.4; 12.4.1		
Estimated Efforts	266 Men*months		
Exercise	Validation Technique	Platform	Exercise Completed
EXE-05.06.04-VP-187	RTS	ENAV Rome	June 2011
EXE-05.06.04-VP-187bis	RTS	LVNL Schipol	August 2011
EXE-05.06.04-VP-188	RTS	NATS London TC	October 2011
EXE-05.06.04-VP-189	RTS	NORACON Malmö	December 2011

i4D + Controlled Time of Arrival

Achievement	Validated procedures, requirements, prototypes and cases for both En-route and TMA environments covering: • Computed and predicted Controlled Time of arrival features exchanged between aircraft and ground using initial 4Dimension capability in traffic synchronisation; • - Impacts on cockpit integration and human factors.			V3
Deliverables	OSED, SPR, INTEROP, Technical Specifications, Validation report			
Contributing Projects	4.3; 9.1 ; 10.7.1			
Estimated Efforts	780 Men*months			
Exercise	Validation Technique	Platform	Exercise Completed	
EXE-04.03-VP-323	Flight Trial	ECTRL MUAC & AIRBUS Flight Test Aircraft	December 2011	

2.2.5 Operational Package 5 Achievements

PAC05 Integrated and Collaborative Network Management

Complexity Assessment and initial Complexity Resolution				
Achievement	Validated procedures, requirements, prototypes and cases for a complexity prediction tool based on: • controller capabilities to solve different complex situations in the airspace, but also possible controller resolutions in the traffic prediction through continuous simulations; • breaking down the predicted complexity/workload in its constituent components, i.e. workload caused by coordination, workload caused by predicted conflicts etc.			V3
Deliverables	OSED, SPR, INTEROP, Technical Specifications, Validation report			
Contributing Projects	4.7.1; 10.8.1			
Estimated Efforts	154 Men*months			
Exercise	Validation Technique	Platform	Exercise Completed	
EXE-04.07.01-VP-001	Shadow Mode	Eurocontrol MUAC	December 2011	

Enhanced Demand Capacity Balancing and dynamic Demand Capacity Balancing processes			
Achievement	Validated Operational procedures, requirements, cases and CFMU Human Machine Interface (HMI) and Network Operational Plan Portal (NOP) enhancement for Short Term Air Traffic flow & Capacity Management Measures (STAM). STAMs are pre-defined scenarios aimed at improving the traffic flow between ATC sectors in coordination with the CFMU for optimising the related sectors capacities.		V3
Deliverables	OSED, SPR, INTEROP, Technical Specifications, Validation report		
Contributing Projects	7.6.5; 13.1.1; 13.2.3		
Estimated Efforts	271 Men*months		
Exercise	Validation Technique	Platform	Exercise Completed
EXE-07.06.05-VP-314 (Remark : The actual list of ATSU is still to be confirmed)	Live Trial	Eurocontrol CFMU	September 2011
		ATSU unit of Reims	
		ATSU unit of London	
		ATSU unit of Frankfurt or Karlsruhe	
		ATSU unit of Maastricht	

2.2.6 Operational Package 6 Achievements

PAC06 Cooperative Asset Management

Integrated Controller Working Position Airport			
Achievement	Validated procedures, requirements, prototypes and cases for low cost and simple departure data entry panel to be deployed at airfields enabling them to be in electronic communication with CFMU concerning the departure status of aircraft under their control.		V3
Deliverables	OSED, SPR, INTEROP, Technical Specifications, Validation report		
Contributing Projects	12.4.1		
Estimated Efforts	33 Men*months		
Exercise	Validation Technique	Platform	Exercise Completed
EXE-12.04.01-VP-391	Shadow Mode	NATS Southampton	February 2011

EXE-12.04.01-VP-404	Shadow Mode	NATS Southampton	November 2011
---------------------	-------------	---------------------	---------------

Integrated Controller Working Position Route and TMA			
Achievement	Validated procedures, requirements, prototypes and cases for a new Human Machine Interface for TMA Controller Working Position (CWP) with improved design, addressing human factors related issues.		V3
Deliverables	OSED, SPR, INTEROP, Technical Specifications, Validation report		
Contributing Projects	5.9; 10.10.3; 10.10.2		
Estimated Efforts	403 Men*months		
Exercise	Validation Technique	Platform	Exercise Completed
EXE-05.09-VP-356	RTS	ENAV	October 2011
EXE-05.09-VP-148	RTS	DSNA	December 2011

Remote Tower			
Achievement	Validated procedures, requirements and prototype for provision of ATC Services on a single airport from a remote site		V3
Deliverables	OSED, SPR, INTEROP, Validation report.		
Contributing Projects	6.9.3		
Estimated Efforts	87 Men*months		
Exercise	Validation Technique	Platform	Exercise Completed
EXE-06.09.03-VP-056	Live Trial	NORACON Ängelholm Airport	November 2011

2.3 Work Package(s) and Projects activities with horizon beyond 2011

SESAR Release 1 is mainly bottom-up driven. Subsequent SESAR Releases will have to incorporate progressively additional top-down guidance as elaborated by SESAR Transverse projects, and in particular performance assessment guidance. The top-down approach will be strengthened through the amount of evidence gathered at future various reviews and taking into account how the projects develop and the level of maturity reached by the

operational and technical solutions. Once a Release is defined, the contributing projects will be synchronised and monitored accordingly.

The R&D results of a SESAR Release will be integrated to become input to WP C Master Plan Maintenance (i.e. the basis for future deployment planning).

During 2011, around 230 projects which are planned to deliver validated results in following Releases will:

- follow their project plan aligned with the E-OCVM methodology and be controlled through the project Gates,
- contribute to the definition of further releases.

In addition, following a procurement procedure initiated in 2010, it is expected that the R&D activities covering the scope of Flight and Wing Operations Centres / Meteorological Services (WP11) will be awarded and executed as an integrate part of the Programme starting in 2011.

All these projects are expected to submit the deliverables listed in their project Initiation Reports (PIRs), with different levels of maturity, including V1 and V2. The SJU will monitor through the Control Gate mechanism the advancement of the projects, the timing and quality of the deliverables to ensure that these projects will be included in their expected Releases, according to the V&V roadmap. A list of the deliverables expected during 2011 is attached as Annexe I⁸.

The effort committed by the Members for these projects during 2011 is estimated at 12.000 Men*months.

The current version of the V&V roadmap provides initial information related to the delivery of the 2012 and 2013 results. The roadmap will be further refined in 2011 to cover as far as possible Step⁹ 2 and Step 3 as well as to contain more precise information for 2012 and 2013; together with R&D results of Release 1, it will then be used as the primary input for the next Releases.

The definition of Release 2 will start early 2011 based on the Validation and Verification Roadmap for Step 1. The scope and schedule will be defined using the same approach as for the first one. The scope of Release 2 will be more ambitious than Release 1 and should address among others, the following topics:

- GBAS
- Time Based Spacing
- Surface Safety Nets
- Full PRNAV
- Advanced Continuous Descent Approach & Continuous Climb Departure
- Initial 4D and Flight Object
- En-route Arrival Management
- Multi-airport arrival Management
- Surface Routing

⁸ The list of the deliverables is based on the projects entered in Execution Phase before 18 November 2010.

⁹ The Step concept is defined in the Concept Storyboard document submitted to the ADB and derived from the Service Level 2 of the ATM Master Plan.

- Complexity Management
- Integrated Network Operations Plan
- Advanced FUA
- Airport AOP

The locations of the expected validation sites for Release 2 and onwards are illustrated on the Figure below.

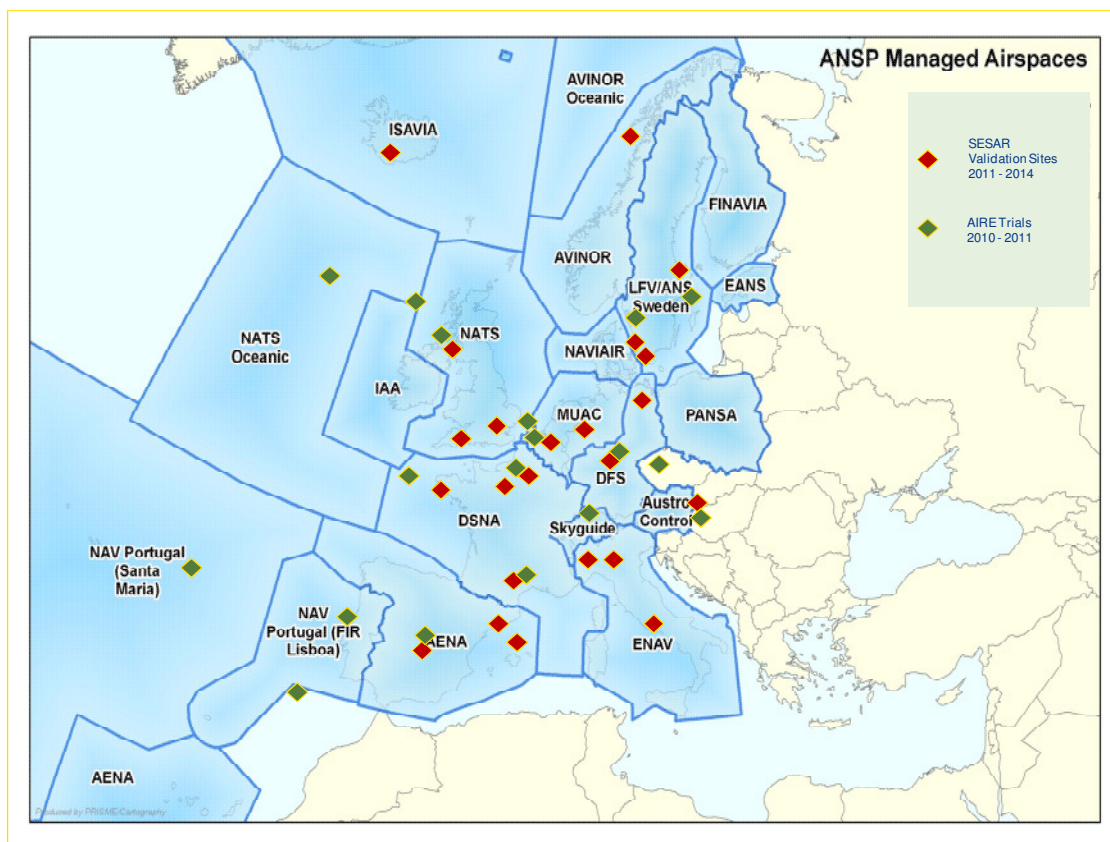


Figure 6: Main locations validation activities for Release 2 and onwards.

3. SESAR Programme Specific Activities in 2011

3.1 Atlantic Interoperability to Reduce Emission (AIRE)

AIRE was established by the European Commission and the US Federal Aviation Administration (FAA) in 2007. The SJU is responsible for its management on the European side since 2008. In 2009 and 2010, having performed 1.152 trials with 18 partners, the AIRE programme was successful in demonstrating that significant environmental savings as CO₂ emission reduction can be achieved at present using existing technology through efficient partnership. Several of the trialled procedures are being applied on the daily basis e.g. CDA procedures in Stockholm or Cruise Climb procedures in Santa Maria (Portugal).

AIRE constitutes a core element of the SESAR Programme. In AIRE national and regional partnerships on tangible, interoperable, “win-win” operational efficiency topics are fostered. Partners, jointly validate solutions that reduce CO2 emissions in the short term and capitalize on present aircraft capabilities.

In 2010, the SJU issued a call for tender and received a large number of project proposals. Eighteen were selected according to the established criteria - in particular projects entailing significant environmental benefits and strongly focusing on implementation - resulting in a significant enlargement of the programme’s geographical coverage and partners. Two projects cover surface operations; five will be carried out on the Terminal Area; four projects for oceanic/en-route procedures; and seven will conduct gate to gate trials involving more than 40 partners.

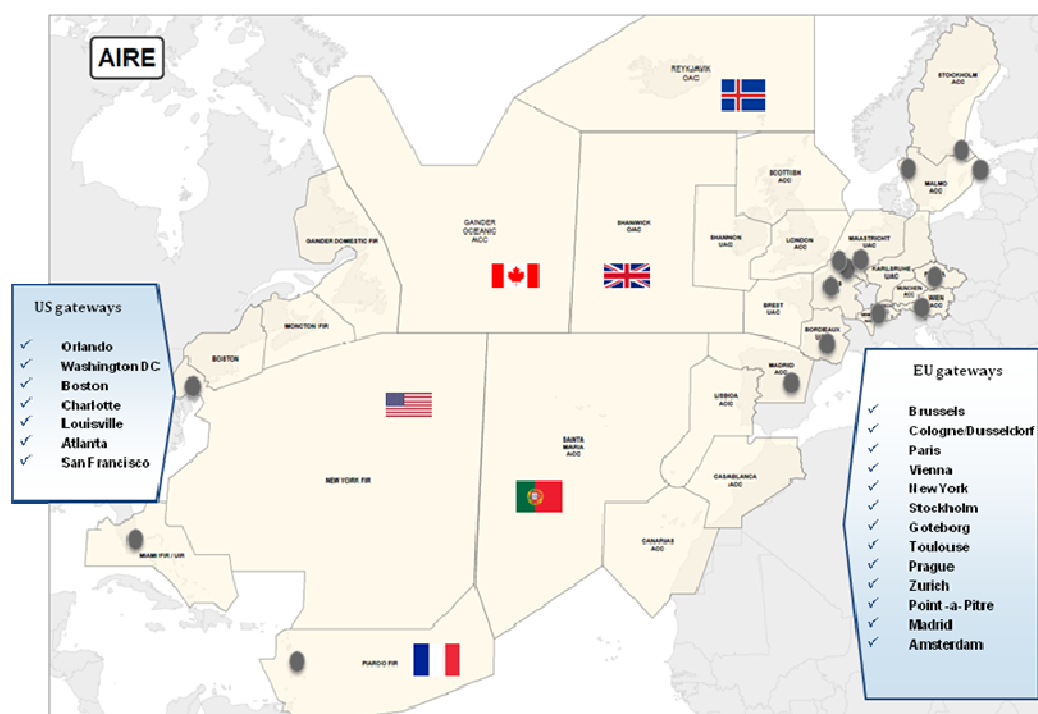


Figure 7: AIRE locations for airports and/or ANSPs

The SJU will closely monitor and evaluate the project plans during the end of 2010/ first quarter of 2011 with the majority of the trials taking place during 2011. More than 2000 flight trials are expected.

Every project has two mandatory deliverables, a Phase1 report describing in details the solution that will be subject to the proof-of-concept, and a final report detailing the findings that can be derived from the validation exercise and possible deployment scenarios.

Insights developed on the basis of the 2009/10 AIRE activities and trials provided a fundamental input to the other Work Packages of the SESAR Programme allowing an earlier deployment of green procedures. Work will continue to further promote the

implementation of tested procedures locally, regionally and at international level. In 2010 a closure technical workshop was organised showing the importance of the synergies between the AIRE activities and those of many of the remaining Programme's Work Packages. These synergies will be further developed in 2011 capitalising on the testing opportunities of AIRE to validate some of industrialisation ready technical solutions being developed in the SESAR Programme. Efforts in 2011 will also be concentrated in considerably expanding the programme in order to impact more locations, stakeholders and further accelerate the pace of change.

Budget 2011	Commitment	Payment
Chapter 3.1 - EUR Mio		
AIRE Phase 2	<i>committed in 2010 for 2.7</i>	1.8
AIRE Expansion	4.8	0.6

3.2 Work Package E

The objective of the SESAR Research Networks is to develop exchange and disseminate knowledge in their field of excellence, by the organisation and successful outcome of a SESAR collective research event.

During 2011, both Research Networks on '*Managing Complexity Safely*' and '*Towards Full Automation in ATM*' will announce their first tranche of funded PhD subjects and the respective host institutions. The main objectives are:

- White papers for strategic Research directions in their domain;
- Annual Joint Workshop (dissemination event);
- Summer Schools;
- Growing participation and review of the activities.

The third Research Network, '*Economics & Performance*', will be launched in 2011, assuming a suitable network proposal is received and selected in November 2010.

With three Research Networks launched this will conclude the first phase for research networks as they move into establishing themselves and preparing for performance assessment in 2012.

A Research Networks combined event will be held during the year, bringing together over 100 different Research organisations spread across the three thematic areas already defined.

2011 will see the launch of the WPE Research Projects (co-funded activities that fall outside of the mainstream development Programme) selected as part of the first call that closed in October 2010. These projects will be committed, initiated and then moved into execution during the year. A further call for Research Projects is planned for 2011 against an updated set of Research Themes; the thematic document will be prepared in collaboration with the SJU Scientific Committee in preparation for the call.

Budget 2011	Commitment	Payment
Chapter 3.1 - EUR Mio	3.5	3.5

3.3 OPTIMI and SAT OPTIMI

In February 2010, after an open call for tender, the SJU launched the OPTIMI (Oceanic Position Tracking Improvement and Monitoring) project, a European initiative for flight tracking in oceanic and remote areas. 13 ANSPs, Airlines, Engineering and manufacturing companies and an Air Transport Communications provider (SITA) have been involved. OPTIMI delivers a set of recommendations which could result in concrete benefits for a number of actors, including Search and Rescue services, accident and incident investigation services, Air Navigation Service Providers and airspace users.

To complement the results achieved so far, the SJU signed a contract on SAT-OPTIMI, after an open call for tenders. SAT-OPTIMI is a study that uses the output from OPTIMI to present the feasibility and options for the best use of satellite infrastructure and technology to ensure full deployment of oceanic and remote tracking services. The study will report by April 2011 and include, among other things, the timing, investment and operations cost estimates, as well as a business and service model for tracking services, giving a clear direction on a path for deployment of aircraft tracking services over oceanic, continental and polar regions

In the light of results from OPTIMI and SAT-OPTIMI, the SJU may propose to conduct complementary work, in particular in the development of specific operational procedures.

Budget 2011	Commitment	Payment
Chapter 3.1 - EUR Mio	<i>committed in 2010 for 0.1</i>	0.1

3.4 ATM Master Plan update

In 2009, the Council of European Union adopted a resolution on the endorsement of the European ATM Master Plan, requesting, inter alia, the European Commission to report annually to the Council on the execution of the ATM Master Plan. The first update of this master Plan was issued and endorsed in March 2010.

The ATM Master Plan contains all the necessary elements to develop and deploy all the SESAR technologies and procedures. The SJU has the competencies, under the Council Regulation (EC) 219/2007, for the execution of the ATM Master Plan. Work package C is the instrument foreseen within the Programme to ensure the maintenance of the European ATM Master Plan and the monitoring of the progress related to the development and the deployment of SESAR.

WP C is organised in 3 pillars: C1 - Master Plan Maintenance, C2 - Performance Deployment Planning, Financial incentives and Reporting, and C3 - Maintenance of Standardisation and Regulatory roadmap. Following the launch of C2 and C3 activities in the execution phase

in early December 2010, the work for the continuous maintenance of the Master Plan will begin.

C2 project kicked-off in October 2010 and will deliver by the end of February 2011 its first milestone: an alignment of the three levels of the European ATM Master Plan to ensure full coverage of the Master Plan in the ESSIP (Eurocontrol Single Sky ImPlementation). This analysis will result in recommendations for mitigating any misalignment. This first milestone will set up a sound and realistic short/medium term baseline to monitor the deployment of SESAR outcomes.

Between March and June 2011, C2 will initiate its deployment reporting and monitoring functions, in order to build short-medium term Deployment Scenarios. The Deployment Scenarios will contain the Deployment Packages. These elements consist of groupings of deployment sequences of SESAR technologies and procedures, defined by a positive business case. Each Deployment Package must demonstrate benefits to the involved stakeholders when deployed. It will also allow the identification of specific measures for those stakeholders which might require particular actions to ensure an overall positive business case for the Package.

The Deployment Scenarios will be the tool to manage SESAR deployment at several geographical levels (pan-European, Regional and National) and per stakeholder group. It will also allow the SJU to perform before the end of 2011 a comprehensive gap analysis (current versus planned situations) and to issue recommendations at technical, operational, financial and regulatory levels to mitigate the risks arising from existing gaps.

C3 projects will also start delivering at high pace and is expected to develop by the end of February 2011 a first Standardisation Roadmap. This Standardisation Roadmap is expected to feed, as regards the SESAR programme, the discussions in different standardisation fora, including the ICAO standardisation roundtable.

C2 and C3 first deliverables will constitute major inputs to the Master Plan update campaign to be launched by C1 after summer 2011. The objective of the Campaign is to prepare a proposal for a comprehensive update of the European ATM Master Plan. It is expected that this update will be a significant one in consideration of the introduction of the Deployment Packages. Wide expert consultation in various domains, including Airspace Users, National Authorities, the Military, and stakeholders from non European States will ensure the necessary inputs and support. During the campaign the Risk Management Plan will be updated based on inputs from the projects.

Budget 2011	Commitment	Payment
Chapter 3.3 - EUR Mio	<i>see WP C</i>	<i>see WP C</i>

3.5 Military

In 2011, the Military Engagement Plan for SESAR (MEPS), drafted by Eurocontrol, is expected to be put in place and become fully operational. The MEPS will enable the full participation of national military authorities in all relevant aspects of the work

programme, via a structured organisation including the formation of specific panels to collate all military input in specific technical or operational domains.

It is expected that the SJU launches a call for tender in order to make an inventory of existing and future military state of the art technologies, in particular for airborne equipment, and their respective performance capabilities. This study will in particular highlight how to ensure interoperability between military and civil technologies, in order to reduce implementation cost for SESAR.

Budget 2011	Commitment	Payment
Chapter 3.1 - EUR Mio	1.0	0.8

3.6 Professional Staff Association

The Professional Staff Associations: ECA, IFATCA, ETF, ATCEUC and IFATSEA have all been contracted by Eurocontrol on behalf of the SJU through a Framework Contract with Annual Work Orders. They participate in the SESAR Programme depending on their professional skills and interest in most of the work packages and projects. The framework contract and the work orders are followed up in quarterly meetings with the SJU and Eurocontrol.

The SJU has agreed with Professional Staff Associations to create an International Validation Team of operational experts, from different nationalities, across all the exercise domains. The team will be fully operational in time for the first validation exercise during 2011.

Budget 2011	Commitment	Payment
Chapter 3.1 - EUR Mio	0.4	0.4

3.7 National Supervisory Authorities

NSAs, Civil and Military, are involved on a regular basis to provide advice on the progress of the SESAR Programme to facilitate the future implementation of the results and anticipate possible issues stemming from it. A Memorandum of Understanding for the provision of expertise has been signed by seven Authorities, covering a comprehensive pan-European geographical scope. During 2010 experts received a detailed picture of the SESAR Programme and agreed on a set of joint activities to be developed in 2011. Work will focus in particular on the regulatory assessment of Release 1 activities, including "Remote & Virtual ATC towers". A significant involvement of NSAs is also foreseen in the review of WP16 deliverables (in particular safety, environment and security assessment methodologies).

The SJU will organize quarterly meetings in 2010 to review the status of the tasks supported by the experts of the Authorities.

Budget 2011	Commitment	Payment
Chapter 3.1 - EUR Mio	<i>committed in 2010 for 0.7</i>	0.2

4. Coordination with other Programmes and Organisations

4.1 FAA/NextGen

During 2011 the EU/USA Memorandum of Cooperation (MoC) is expected to be formally adopted providing a political and legal framework allowing the SESAR/NextGen Annex on interoperability to become effective. The MoC identifies 5 headline areas of cooperation:

- Transversal Activities,
- Information Management,
- Trajectory Management
- CNS & Airborne Interoperability,
- Collaborative Projects.

Working Groups will be established for each of these cooperation areas and their activity will focus on the definition of actions and outputs to ensure that appropriate coordination is achieved.

A set of priority subjects for cooperation with the FAA has been identified; these high priority subjects required for harmonisation and interoperability include the definition and exchange of 4D trajectory, Aeromacs/Wimax profile definition, ADS-B applications, GNSS configurations and convergence of the overall concept of operations where it impacts on interoperability.

The modus operandi of each Working Group is to engage the SJU Members in the work where practicable and have this work included within projects already in the SESAR Programme. Hence there will be no need for a parallel programme of activity on interoperability issues with the US due to this inclusive and integrated approach.

The key principles underlying the interoperability cooperation work are:

- SESAR/NextGen technical cooperation is integrated within the Programme and that coordination activities are mainly allocated to SESAR contributing partners;
- All coordination activities must show demonstrable value, clear deliverables and alignment with a committed timescale;
- SESAR partner activities will be managed and reported via existing project and programme management arrangements with both Working Group Leaders and a Coordination Committee ensuring compliance with the Annexe.

Additional areas of technical and operational coordination will also be established in future. Strong and effective cooperation is expected to produce concrete results for input into the work programme.

Budget 2011	Commitment	Payment
Chapter 3.3 - EUR Mio	<i>part of the Programme costs</i>	<i>part of the Programme costs</i>

4.2 Clean Sky

Clean Sky includes within its scope two aspects of key interest for SESAR: the airborne flight management and trajectory aspects as well as environmental modelling to demonstrate what improvement is expected from the Clean Sky technology developments. SESAR has a complementary environmental programme of work in AIRE and environmental modelling for the programme in Work Package 16 as well as development of Airborne FMS/Avionics and communications improvements in Work Packages 9 and 15.

Consequently, the SJU has already established direct links between the Work Package 9 and Clean Sky and during 2011 this is expected to realise an exchange of information ensuring that SESAR developments are aligned with and encompass the forthcoming changes in aircraft performance and operations.

During 2011 the SJU intends to ensure alignment of modelling assumptions and methods between the SJU WP 16 and the Clean Sky Technology Demonstrator in order that claims for environmental improvements are expressed consistently.

Budget 2011	Commitment	Payment
Chapter 3.3 - EUR Mio	<i>part of the Programme costs</i>	<i>part of the Programme costs</i>

4.3 Framework Programme (FP) Projects

During 2010 the SJU have established regular coordination meetings with both DG MOVE and DG RTD and have collated a list of active and new framework projects. During 2011 coordination between relevant projects in SESAR and the Framework Projects identified as relevant to the Programme will be activated to ensure the SJU is '*coordinating and concentrating all European Union's relevant research and development efforts in ATM*'.

During 2011, for the new Framework Projects not already selected, the SJU will, offer to directly support DG RTD in the selection activities to ensure that proposals do not duplicate what is already scoped and funded in the SESAR work programme.

4.4 ICAO

The SJU has participated already in 2010 in the Standardization Roundtable that coordinates the standardization needs of NextGen and SESAR under the umbrella of ICAO.

At least two other meetings of this group are foreseen during 2011 with the target of producing a common set of roadmaps and identifying near-mid -term standardisation needs ready for presentation to the ANC12.

Later it is envisaged that this forum will evolve into a more strategic monitoring group. There is a strong connection between the work in this scenario and the development and maintenance of the Standardization Roadmap under WP C.

The ICAO near-term standardisation needs will be directly mapped into the SESAR Programme activities in order to ensure that there is appropriate provision for the standards required by the concepts and technologies being developed in the programme. Gaps and overlaps will be identified in order to provide updates to the ICAO planning.

Besides the Standardization field, ICAO has been and will continue to be involved in OPTIMI through their participation in the OPTIMI Supervisory Committee. The technical and operational involvement of stakeholders from non-European States in this type of SESAR initiatives will be ensured through ad hoc and limited participation in regional groups. In particular, a Working Paper will be presented by the SJU in the GREPECAS plenary meeting in March 2011.

Finally, there is a great interest from the global aviation community to count on a strong presence of SESAR in the ICAO Air Navigation Conference that will take place in 2012. Preparation of the ANC12 is a key target in terms of supporting a globally harmonised planning which is consistent with the work of SESAR.

4.5 EASA

EASA and the SJU have agreed on how to ensure effective involvement of EASA, with the support of Eurocontrol as deemed necessary, in the Programme in respect of ATM safety issues. Before the beginning of each year, EASA will receive from the SJU and approve the plan with the deliverables scheduled for the following year.

4.6 ESA

The SJU and ESA, through the IRIS programme, have already established a productive working arrangement where ESA staff actively participates in SJU projects relevant to them, and SJU staff and project participants meet to exchange relevant information. The SJU also participate directly to the Joint Iris Advisory Committee. These activities will continue in 2011 and become focussed on developing a recommendation to be presented to the SJU Administrative Board on the further deployment of Iris as a means of satisfying the satellite component in SESAR's communication needs.

4.7 External relations

The SJU pursues international relations in the context of the European Commission external relations framework. This has included support to the Commission in extending SESAR to the Latin American States. In this context, in 2011 SESAR aims at consolidating technical cooperation with Brazil and at providing support to the EC for the initialling of a Memorandum of Understanding with Mexico. Using Optimi-Aire-like initiatives, exploration of possible bilateral relations with the East African States (Atlantic States) is also being considered. Apart from that, follow-up on SESAR workshops held in Turkey and the Ukraine as well as further developments and maintenance of relations with Southern

Mediterranean States is also foreseen. Work will continue with China, India and Middle East Countries.

Overall, the SJU maintains an opportunistic approach to external relations, ensuring the highest benefit for the future Programme deployment and its Members.

5. Communication plan

The success of the SJU and the achievement of the SESAR Programme results depend from a proper communication of the correct messages to the staff involved in the Programme, to the SJU stakeholders and to the Air Transport community at large and the general public as well.

In this respect the “*Communication Plan SESAR JU*” has been established and approved by the ADB in 2009. Based on the lessons learnt from 2010, the Communication activities for the 2011 will strengthen the first results of awareness and proactive information attitude achieved so far. In 2011, different actions detailed in the Communication Plan will be performed:

- Joint communication activities with the SESAR Members & Associate Partners;
- Intense internal communication to the 2.000 SESAR dedicated staff;
- Strong presence at ATC Global Amsterdam for the second time with several conferences and workshops to inform the audiences on the SESAR WP progresses;
- Regular on-line communication + internal & external newsletters;
- Enriching databases to reach new air transport stakeholders;
- -Selective participation at major conferences on ATM & Air Transport;
- Updated communication tools such as website, brochures, videos, etc
- Second communication action towards passengers at airports;
- Communication activities about the programme AIRE.

Budget 2011	Commitment	Payment
Chapter 2.3 - EUR Mio	0.3	0.3

6. Administration & Finance

6.1 Ensure efficient support to the Programme implementation

With the finalisation of the BAFO II, the assignment of work to the Members is almost completed; in 2010 the SJU has assigned the work concerning the WP11 and WPE. In 2011 almost all the Programme’s projects will be in the execution phase. The Directorate of Administration & Finance will continue its efforts to support the Programme implementation by ensuring the timely availability of the necessary resources, human and financial, and by providing the necessary internal control aiming at the respect of the principle of sound financial management and the legality of the underlying transactions.

Between the critical activities, the Directorate will organize the expected IBAFO III, will follow up the completion of the “Associate Partners of the SJU” call and will ensure the amendment of the MFA to incorporate the results of the initiation phase.

6.2 On time assessment of Contractual Deliverables and Project’s Interim Report.

By the end of 2011 the SJU will have pre financed almost all the Programme projects with an overall disbursement of about EUR 143.6 million since 2009. Eligible costs referring to projects having completed the initiation phase are co-financed according to the provisions of the MFA.

Interim report will be provided in June 2011 including eligible cost incurred by the Members during 2010; internal procedures ensure that the operational and financial requirements are satisfied in respect of the acceptance of contractual deliverables.

According to the provision of the MFA, the projects co-financing is granted to the Member on the basis of the Certified Interim Financial Statement referring to the incurred costs related to accepted deliverables and work in progress. In this respect and on the basis of the Certified Interim Financial Statement, the SJU plans to disburse EUR 70 million to the Members as co-financing.

The deliverables acceptance and the payment authorisation processes are defined in the Financial Circuits ensuring full compliance with the terms of the Financial Rules necessary to receive financing from the European Union budget.

Financial Initiation and Verification functions are performed respecting the four eyes principle with a clear separation of responsibility; the process is supported by the use of the ABAC system. The delegation of authority for budget implementation and the assignment of Initiating and Verifying functions to staff ensure the necessary resources to implement the processes providing adequate segregation of functions and accountability of the actors involved.

6.3 Ensure effective implementation of ICS and risk management

The Programme implementation and the increasing disbursement of funds call for a further strengthening of the internal control. The Administrative Board has approved in 2010 the SJU’s Internal Control Standards for effective management derived from the communication of the European Commission “*Revision of the Internal Control Standards and Underlying Framework Strengthening Control Effectiveness*” SEC (2007) 1341. This provides the SJU’s management and staff with a clear set of standards to comply with in performing their activity.

Furthermore within the SJU Risk policy a corporate approach is implemented with the objective of providing the SJU with a Risk Management system which addresses the

uncertainty related to the achievement of its objectives. The adoption of a common model builds on three basic concepts:

- Risk management is a continuous process which develops at different level of responsibilities within the SJU;
- Risk management is linked to the SJU's strategy which includes a clear risk policy to determine its risk appetite;
- Risk management is a process that identifying potential events affecting the ability of the SJU to reach its objectives, allows the management to take actions and define mitigating measures giving them reasonable assurance on the achievement of the objectives.

Building on the first results achieved and on the findings of the 2010 Risk Report, the SJU will further develop in 2011 the Risk management system. This is in line with the requirements of the European Commission concerning risk management contained in the Communication SEC (2005) 1327.

6.4 Set up Programme's financial audit structure

The Project Audit Sector, will support the Members to achieve the overarching result of maximising the benefit of the resources available for the Programme by raising awareness of best practice, guiding in the better implementation of the SJU Rules, MA, MFA and contributing to the proper, economic, efficient use of the resources.

The administrative support to the Programme implementation, reinforced in 2010 through the recruitment of two Projects Auditors in charge of ex post project audit, will be fully deployed in 2011 adding further assurance on the use of funds. In strict cooperation with operational functions, the Projects Auditors are responsible for checking the compliance with the principle of sound financial management and in particular to assess deliverables' value for money. The Ex-Post Project Audit Strategy, expected to be approved by the ADB in December 2010 will be implemented with the support of a provider of audit services to whom a contract has been awarded.

At the beginning of 2011, the Project Audit Annual Plan will be established and submitted for approval to the Executive Director.

The Plan will contain the project audits to be performed

- At least 5 Members and 2 Service Contracts determined either through a statistical approach or on a risk based approach;
- Additional audits as required by the SJU management taking into consideration different relevant elements.

7. Internal Audit

7.1 Internal Audit Work Programme 2011

The Administrative Board will be invited to approve the Internal Audit work program for 2011. It will be established on the basis of an updated analysis of risks faced by the SJU in its research and development program operations and the risks inherent to its specific nature as a European Union Body charged with the execution of a public private partnership.

7.2 Changes to the SJU internal audit arrangements in 2011

In 2010 the European Court of Auditors considered that there are strong arguments in favour of allowing the same powers for the Commission's Internal Auditor as exercised in respect of other EU bodies¹⁰. In response the Internal Auditor of the European Commission wrote to the SJU Administrative Board Chairman and Executive Director informing of his intention to undertake the responsibility of being the SJU Internal Auditor. The Administrative Board will be invited to approve measures to realign the SJU Internal Audit function to establish an Internal Audit Capability and to recognize formally the role of the Internal Auditor of the European Commission as the SJU Internal Auditor.

7.3 Assurance work

Emphasis will be placed on assurance work designed to enable the Executive Director to report on the SJU system of internal control in the context of the execution of the SJU work program and its associated budget following the successful ramp-up phase in 2010. Assurance work will be largely undertaken by the newly established SJU Internal Audit Capability in 2011.

7.4 Consulting and other work

In 2011 internal audit consulting effort will include realignment of the internal audit structure and putting in place new working arrangements to support it. Providing consulting advice on conflict of interest management; the operation of the financial circuit; and other aspects of the internal control system will continue to represent around a third of available resources.

7.5 Co-ordination and oversight of public audit functions

The SJU Permanent Audit Panel co-ordinates the activities of the audit and control functions of the SJU's Founding Members and advises the Administrative Board on audit

¹⁰ European Court of Auditors, Opinion No. 2/2010 on the SESAR Joint Undertaking Financial Rules.

related matters. In 2011 the Panel's rules of procedure will be adapted to reflect the new internal audit structure.

7.6 Resources

The SJU Internal Audit Capability will retain one full-time internal auditor seconded from Eurocontrol. Additional specialist expertise may be purchased externally in 2011 where this is deemed necessary or appropriate. In 2011 further efficiency gains from the use of audit tools and guidance on audit methodology provided by the Commission Internal Audit Service are expected to offset the effort of establishing the new internal audit structure. Therefore resource requirements in 2011 are expected to be maintained at the level of 2010.

8. Glossary

4 D	4 Dimensions
ABAC	Accrual Based Accounting
ACAS	Airborne Collision Avoidance System
A-CCD	Advanced Continuous Climb Departure
A-CDA	Advanced Continuous Descend Approach
ADS-B	Automatic Dependence Surveillance-Broadcast
ADS-C	Automatic Dependence Surveillance-Contract
AeroMacs	Aeronautical Mobile Airport Communications System
AFUA/ASM	Advanced Flexible Use Airspace/Airspace Management
AMAN	Arrival Manager
ASPA	Airborne Spacing
ATM	Air Traffic Management
ATSA ITP	Air Traffic Situation Awareness- In-Trail Procedure
CCD	Continuous Climb Departure
CDA	Continuous Descend Arrival
CDM	Collaborative Decision Making
CNS	Communication, Navigation, Surveillance
CTA	Controlled Time Arrival
DCB	Demand and Capacity Balancing
DCMAC Euroc.	Directorate Civil Military ATM Coordination
DMAN	Departure Manager
GBAS	Ground Based Augmentation System
GNSS	Global Navigation Satellite System
I 4D	Initial 4 Dimensions
I CWP	Integrated Controller Working Position
IOP	Inter Operability
LVP	Low Visibility Procedure
MSP	Multi Sector Planning
NOP	Network Operation Plan
OAT	Operational Air Traffic
P-RNAV	Precision Area Navigation
RNP	Required Navigation Performance
RTS	Real Time Simulation
S&M	Sequencing & Merging
SBT/RBT	Shared Business Trajectory/Reference Business Trajectory
STCA	Short Term Conflict Alert
SWIM	System Wide Information Management
TMA	Terminal Area
UDPP	User Driven Prioritisation Process

9. Annexe I - Projects (excluding Release 1) in Execution Phase - 2011 Planned delivery

10. Annexe II - Programme Financials
